

Breadfast Neverland Recovery Plan

Belal Bahr

1nd of July, 2025

1. Executive Summary

One year after launching in Neverland, Breadfast is operating at only 50% of its expected daily order volume. This underperformance caused an internal review to identify root causes and define a path forward.

The investigation revealed three key issues:

1. **Long delivery times** affecting customer satisfaction and retention.
2. **Low brand awareness** limiting customer acquisition in the new market.
3. **Complex app user experience** reducing order completion rates.

To address these, a targeted action plan was developed that includes improving delivery logistics, launching localized marketing campaigns, and redesigning critical parts of the app. Each action is tied to specific metrics and owners, with a progress tracker in place to monitor implementation.

Clear success criteria have been defined to measure the impact of each initiative. The project will be considered complete once the target daily order volume is achieved and sustained, supported by improvements in customer satisfaction, acquisition, and retention.

By addressing delivery, awareness, and UX bottlenecks through this structured plan, Breadfast can realign Neverland's operations with growth targets. Continuous monitoring and stakeholder collaboration will ensure sustained success.

2. Breakfast Neverland Performance Improvement Project Charter

2.1 Problem statement:

Breadfast's Neverland operations are generating only 50% of the projected daily order target X one year post-launch. This underperformance impacts revenue, market share, and scalability goals.

2.2 Objectives:

- Investigate and identify root causes of underperformance.
- Implement corrective actions to get back on track.
- Design a tracking system to monitor progress against recovery plan.

2.3 Scope

- Analysis of Neverland operations, marketing, customer experience, and competition.
- Implementation and monitoring of corrective actions in Neverland.

2.4 Key Stakeholders

Table 1. Key Stakeholders involved in improving Breadfast's Netherland Performance.

Role	Title	Responsibilities
Sponsor	Head of Growth	Approves budget and strategic direction.
Project Lead	Program Manager	Oversees analysis, plans execution, and reporting.
Core Team	Marketing Operations Product	Campaign and outreach analysis and improvement. Fulfillment and logistics assessment and improvement. Application UX assessment and improvement.
Support	Data Analytics Team	Assists with data gathering and insights.
External	Neverland Customers	Surveyed and interviewed for feedback.

2.5 Key Deliverables

1. Root cause diagnosis report.
2. Prioritized recovery action plan.
3. KPIs dashboard and progress tracker.
4. Post-implementation review.

2.6 Success Criteria

- Sustained X daily orders for 30 consecutive days.
- Improved customer retention rate.
- Increased customer satisfaction.
- Final report delivered and approved by key internal stakeholders.

2.7 Risks

Data access limitations, market saturation, and budget constraints.

3. Root Cause Analysis

To understand why Breakfast is underperforming in Neverland, a root cause analysis using the Fishbone Diagram was conducted. The 6Ps framework (People, Process, Promotion, Place, Product, and Price) was used to categorize the potential causes accordingly.

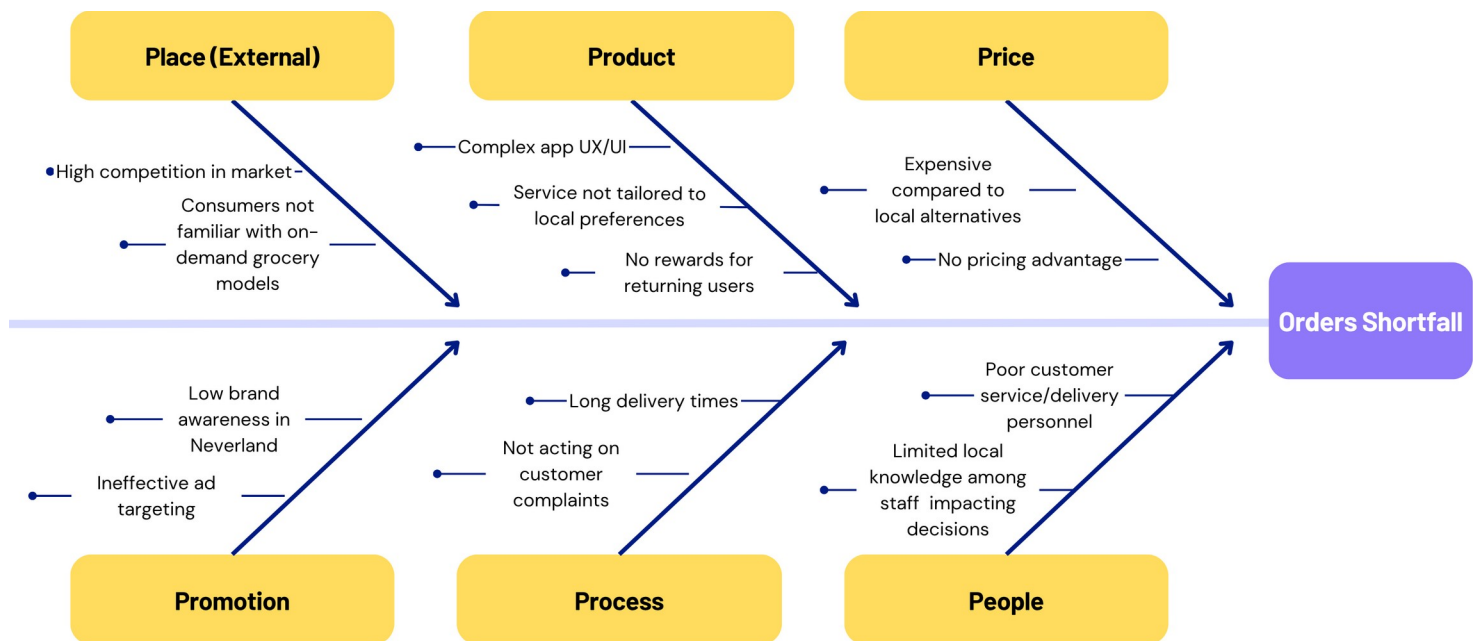


Figure 1. Causes of Orders Shortfall Fishbone Analysis.

This approach strategically maps internal and external causes that could be contributing to our expected vs actual daily orders gap in Neverland.

4. Validation of Hypotheses

To confirm or disprove the potential root causes identified in the Fishbone Analysis, multiple data has to be collected across marketing, operations, customer experience, and the competitive landscape.

To streamline analysis, one representative hypothesis per category was selected to perform the validation testing. Below is a breakdown of the validation process per hypothesis:

People

Hypothesis: Limited local knowledge among staff impacting decisions.

Data required:

- Asses employee's familiarity with local market context:
 - Staff surveys on cultural and regional knowledge.
 - Analysis of staff background: local vs external hires.
- Review decision outcomes against local consumer feedback.
- Review KPIs for decisions in areas with and without strong local input.

Process

Hypothesis: Long delivery times.

Data required:

- Operational metrics on fulfillment:
 - Actual vs estimated delivery times per order.
 - Percentage of late deliveries.
 - Reasons for delays.
- Collect surveys on customer satisfaction related to delivery speed and compare them against targets or competitor benchmarks.
- Logistic data like route distances and driver availability can also diagnose bottlenecks.

Promotion

Hypothesis: Low brand awareness in Neverland.

Data Required:

- Measure brand awareness via market research:
 - Consumer surveys of target audience % recognizing Breadfast pre and post-campaign.
 - Brand recognition tests.

- Social media search volume for "Breakfast" in Neverland vs. competitors.
- Evaluate marketing reach:
 - Ad impression-to-signup conversion rates.
 - Local advertising spend.

Place (External)

Hypothesis: Consumers not familiar with on-demand grocery models.

Data Required:

- Survey local consumer on their shopping habits and channel preferences.
- Study a competitor entry in the region.
- Track adoption metrics:
 - Percentage of local market using similar services.
 - Growth rate over time.
 - Do a segmentation analysis

Product

Hypothesis: Complex app UX/UI.

Data Required:

- Conduct user surveys, interviews, and usability testing to identify issues.
- Create a user journey map.
- Benchmark against UX standards and competitor apps.
- Analyze app usage data:
 - User onboarding success rate.
 - Shopping cart abandonment rate.
 - Orders cycle time.
 - Customer support tickets regarding app difficulties.

Price

Hypothesis: Expensive compared to local alternatives.

Data needed:

- Compare the app's item prices+delivery fees with local store prices and other delivery services.
- Conduct customer surveys on price perception and sensitivity.
- Analyze price elasticity (track order volumes as prices or fees change).

5. Assumptions and Recommendations

Following analysis and hypothesis validation, the following three primary factors contributing to the underperformance in daily orders in Neverland were identified (assumed):

1. Long delivery times

Operational data indicates that delivery lead times exceed customer expectations, especially during peak hours. This negatively impacts customer satisfaction and produces a low customer retention rate.

2. Low brand awareness in Neverland.

Market research and brand recall surveys confirm that Breadfast's brand visibility is significantly lower compared to local competitors. This lack of awareness limits customer acquisition.

3. Complex app UX/UI.

User behavior data and feedback reveal pain points in navigation and checkout within the app, leading to a high cart abandonment rate and lower conversion rates.

Below are targeted recommendations and a structured action plan to address each root cause.

Long Delivery Times

Recommendation: Optimize delivery operations to reduce order fulfillment time and improve reliability.

Action Steps:

1. Route Optimization: implement or upgrade routing software to reduce delivery distance and improve efficiency.
2. Delivery Zone Reassignment: analyze order density and reassign delivery zones to balance workloads.
3. Fleet Expansion: increase the number of delivery personnel or vehicles during peak hours.
4. Performance Monitoring: introduce KPIs such as average delivery time, on-time delivery rate, and route utilization.

Owner: Operations Manager.

Timeline: 4–6 weeks.

Dependencies: operations team, logistics team, IT support, and driver recruitment.

Low Brand Awareness in Neverland

Recommendation: Launch a localized brand awareness campaign tailored to Neverland's customer base.

Action Steps:

1. Targeted Campaigns: launch digital and offline campaigns using localized content and language. Focus on high-traffic channels like social media, local influencers, and hyperlocal media.
2. Referral Program: introduce a “refer-a-friend” incentive for current users to spread awareness organically.
3. Sampling Events: host community activations (e.g., pop-up stands or product sampling) in key neighborhoods.
4. Awareness Tracking: use pre/post surveys and social metrics (reach, engagement, recall) to assess campaign effectiveness.

Owner: Marketing Manager.

Timeline: 6–8 weeks.

Dependencies: marketing team, marketing budget, local partnerships.

Complex App UX/UI

Recommendation: Redesign critical parts of the user journey to streamline app usability and reduce complexity during order placement.

Action Steps:

1. UX Audit: Conduct expert usability testing and A/B testing sessions to identify specific pain points and alternatives.
2. UI Simplification: change the homepage, navigation structure, and checkout flow based on findings.
3. Onboarding Redesign: Create an intuitive first-time user experience with tips and walkthroughs.
4. Metrics Monitoring: orders cycle time, drop-off rate before and after deployment, and CSAT scores.

Owner: Product Manager.

Timeline: 7–10 weeks.

Dependencies: product team, engineering, and app development resources.

6. Tracking Progress

To ensure accountability and timely execution, a Gantt Chart will be used to monitor the implementation of all corrective actions. The Gantt Chart below captures the status of each initiative, highlights key metrics, and supports transparent reporting to key internal stakeholders.

Assuming that gathering data would take two weeks, one week to analyze root cause and form insights, and one week for planning, the schedule of the corrective actions will begin execution in 4 weeks.

AT RISK	Corrective Action	Key Metrics	STATUS	ASSIGNED TO	START DATE	END DATE	DURATION (days)	COMMENTS	STATUS
	Route Optimization	average delivery time, on-time delivery rate	Not Started	Operations Manager	08/03	09/04	33		Not Started
	Delivery Zone Reassignment	delivery load balance, driver efficiency	Not Started	Operations Manager	08/03	09/22	51		In Progress
	Fleet Expansion in Peak Hours	orders per hour, driver availability	Not Started	Operations Manager	08/03	08/26	24		Complete
	Brand Awareness Campaign Launch	reach, impressions, brand recall	Not Started	Marketing Manager	08/03	09/17	46		On Hold
	Referral Program Deployment	new users, referral conversions	Not Started	Marketing Manager	08/18	09/08	22		Overdue
	Community Sampling Events	event attendance, post-event signups	Not Started	Marketing Manager	08/11	09/21	42		Needs Review
	UX Audit and User Testing	usability scores, customer's feedback	Not Started	Product Manager	08/03	08/17	15		Canceled
	UI Simplification	orders cycle time, and drop-off rates	Not Started	Product Manager	08/18	10/09	53		
	Onboarding Redesign	onboarding completion %, time to first order	Not Started	Product Manager	08/18	09/23	37		

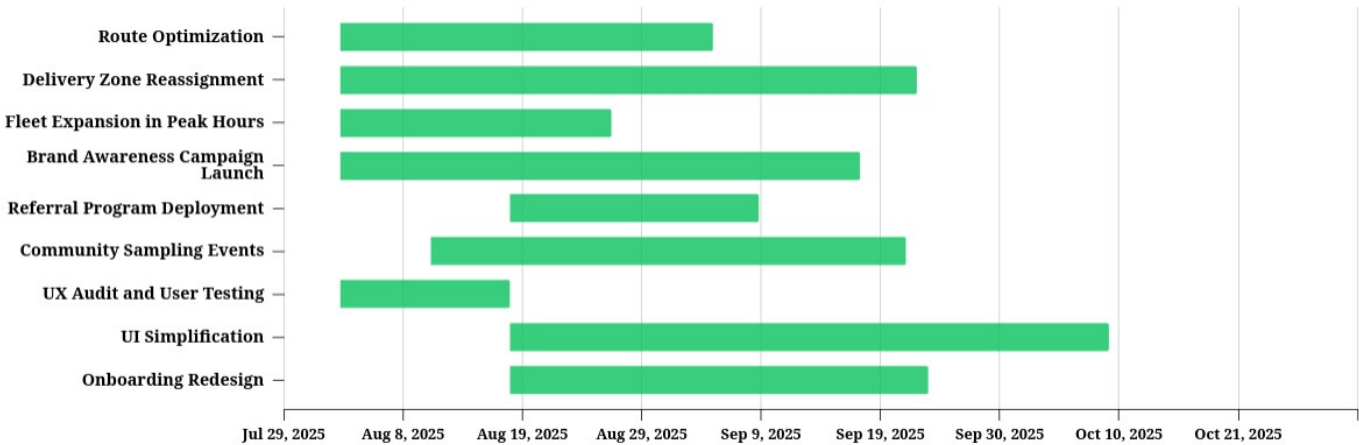


Figure 2. Recovery Plan Gantt Chart

Each action has a single accountable lead to ensure focus and delivery. Department leads will report progress, risks, and blockers weekly. Moreover, a biweekly review will be held to review impact of completed actions and reallocate resources as needed. Consequently, KPI trends will be visualized in a Power BI dashboard shared with project stakeholders.

7. Success Criteria

To determine whether the implemented actions have effectively addressed the root causes and the overall project goals have been achieved, the following success criteria are defined.

These criteria follow the goals of SMART goals principle; they're specific, measurable, achievable, relevant to the project objectives, and time-bound.

Table 2. Corrective Actions Success Criteria.

Corrective Action	Success Criteria	Measurement Method
Long Delivery Times	• Average delivery time reduced by at least X% compared to baseline. • Y% of orders delivered within the promised time window. • Customer satisfaction score related to delivery increases by Z %.	Logistics KPIs, surveys, and delivery time tracking via app.
Low Brand Awareness	• Aided brand awareness in Neverland increases by at least X % in post-campaign survey. • Y% increase in new user acquisition in Neverland region. • Referral usage contributes to Z % of new customer growth within 2 months.	Brand tracking surveys, digital campaign analytics, and CRM data
Complex App UX/UI	• App drop-off rate during checkout reduced by X%. • First-order completion time reduced to under Y minutes for new users. • App store rating improved to at least Z stars within 2 months of update.	App usage data, usability testing metrics, and app store feedback.

Project-Level Success

Overall Objectives:

- Achieve target of **X** daily orders within 3 months of project launch.
- Improvement in key business metrics such as customer retention, average order value, and order frequency.

How they will be calculated:

- Daily order volume reports from Neverland region.
- Comparison of post-implementation metrics to pre-project baseline.

Success will be confirmed when the order volume target is met and sustained for 4 consecutive weeks, alongside improvements in supporting KPIs listed above.

8. Conclusion

Breadfast's performance in Neverland has fallen short of expectations, reaching only half of the projected daily orders after one year. Through a detailed analysis, we identified three main challenges: slow delivery times, low brand awareness, and a complex app experience.

This report outlines a focused action plan to address each issue with practical steps, clear responsibilities, and measurable goals. If implemented effectively, these actions will help improve customer satisfaction, attract new users, and increase order volume.

With close monitoring and cross-team collaboration, Breadfast can get back on track and achieve its growth target in Neverland. Continued evaluation and adjustment will ensure that the solutions remain effective and aligned with customer needs.
